


APPENDIX D

Map and Schedule



ID	Task Name	Duration	Start	Finish	Predecessors	2007	2008	2009	2010	2011	2012	2013	2014
184	Transbay Area Plan & Fourth & King Study Preparation (Consultant-Lead)	520 days?	Thu 5/17/07	Wed 5/13/09									
185	Consultant Hiring	52 days?	Thu 5/17/07	Fri 7/27/07									
186	Issue RFP	0 days	Thu 5/17/07	Thu 5/17/07									
187	Proposals Prepared by Consultant Teams	23 days?	Thu 5/17/07	Mon 6/18/07	186								
188	Pre-Proposal Meeting	0 days	Tue 5/29/07	Tue 5/29/07									
189	Proposals Due	0 days	Mon 6/18/07	Mon 6/18/07									
190	Proposal Evaluation and Interviews	15 days	Mon 6/18/07	Fri 7/6/07	189								
191	Contract Negotiations	15 days	Mon 7/9/07	Fri 7/27/07	190								
192	Consultant Under Contract, Work Begins	0 days	Fri 7/27/07	Fri 7/27/07	191								
193	First Draft	100 days	Mon 7/30/07	Fri 12/14/07	192								
194	Internal Review and Comment	1 mon	Mon 7/30/07	Fri 8/24/07									
195	Draft for Public Review	3 mons	Mon 8/27/07	Fri 11/16/07	194								
196	Public Review of Draft Plan	1 mon	Mon 11/19/07	Fri 12/14/07	195								
197	Planning Commission and Other Public Bodies Review	0.05 mons?	Mon 12/17/07	Mon 12/17/07	196								
198	Final Plan Preparation	3 mons	Tue 12/18/07	Mon 3/10/08	197								
199	Adoption Hearings	3 mons	Thu 2/19/09	Wed 5/13/09	198,219								
200	Transbay Area Plan and Fourth & King Railways Study EIR (Program and Project Level)	448 days	Mon 6/4/07	Wed 2/18/09									
201	Funding Methodology for DEIR preparation (PD CFO and City Attnys)	0 days	Mon 6/4/07	Mon 6/4/07									
202	Consultant Hiring	66 days	Fri 6/29/07	Mon 10/1/07									
203	Preliminary Project Description for EIR RFP (Staff Task, See Above)	0 days	Fri 6/29/07	Fri 6/29/07	170								
204	Issue RFP	0 days	Mon 7/9/07	Mon 7/9/07	203								
205	Proposals Prepared by EIR Consultant Teams	30 days	Mon 7/9/07	Fri 8/17/07	204								
206	Pre-Proposal Meeting	0 days	Fri 7/27/07	Fri 7/27/07	204FS+15 days								
207	Proposals Due	0 days	Fri 8/17/07	Fri 8/17/07	205								
208	Proposal Evaluation and Interviews	15 days	Mon 8/20/07	Fri 9/7/07	207								
209	Select Preferred Consultant	1 day	Mon 9/10/07	Mon 9/10/07	208								
210	Contract Negotiations	15 days	Tue 9/11/07	Mon 10/1/07	209								
211	Consultant Under Contract, Work Begins	0 days	Mon 10/1/07	Mon 10/1/07	210								
212	Project Description (Consultant EIR Task)	2 mons	Fri 6/15/07	Fri 8/10/07	164FS-50%								
213	Transportation Study (See Above)	0 mons	Fri 7/13/07	Fri 7/13/07	169								
214	DEIR Preparation	12 mons	Thu 11/1/07	Wed 10/1/08	212,213FS 33%								
215	DEIR Published	0 days	Wed 10/1/08	Wed 10/1/08	214								
216	Public Review	1.5 mons	Thu 10/2/08	Wed 11/12/08	215								
217	Response to Comments (Best Guess: Schedule Depends on Outcome of Review)	3 mons	Thu 11/13/08	Wed 2/4/09	216								
218	FER	0.5 mons	Thu 2/5/09	Wed 2/18/09	217								
219	Certification-ready	0 days	Wed 2/18/09	Wed 2/18/09	218								
220	Transit Center and Tower Design & Development Competition	1915 days	Thu 1/11/07	Wed 5/14/14									
247	Other Transbay Participating Projects	618 days	Sun 1/28/07	Wed 6/10/09									
255	Other Related Projects (Other Agency Leads)	420 days	Sat 1/20/07	Fri 8/23/08									
274													

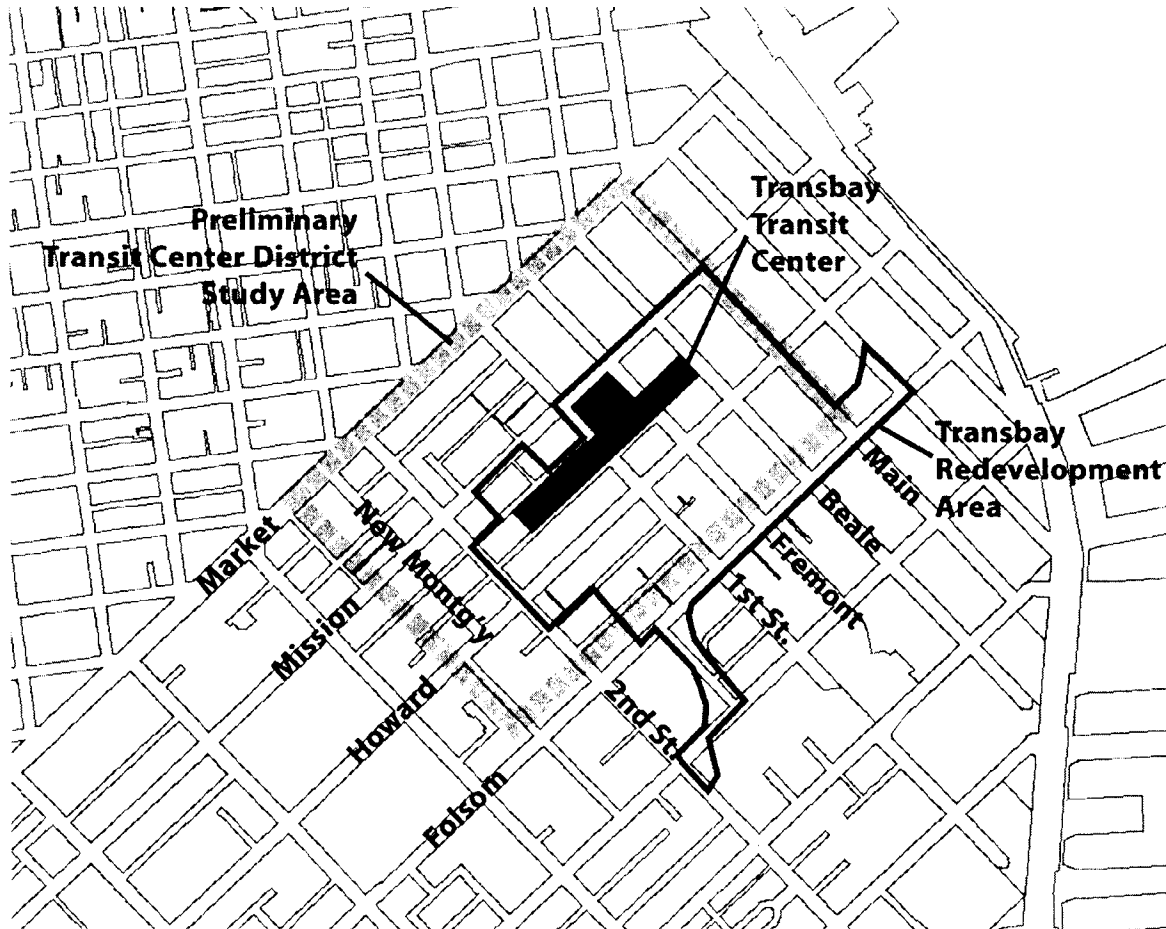

Split

External Tasks

External Mile Task



Summary

Project Summary

Progress

Milestone



Task

Split

Task

Split

Task

Split

Task

Split

Task

Split

Task

Split
